Fri 18/09/20

Whitwick and Coalville Leisure Centre - Summary Construction Programme

building & project consultants
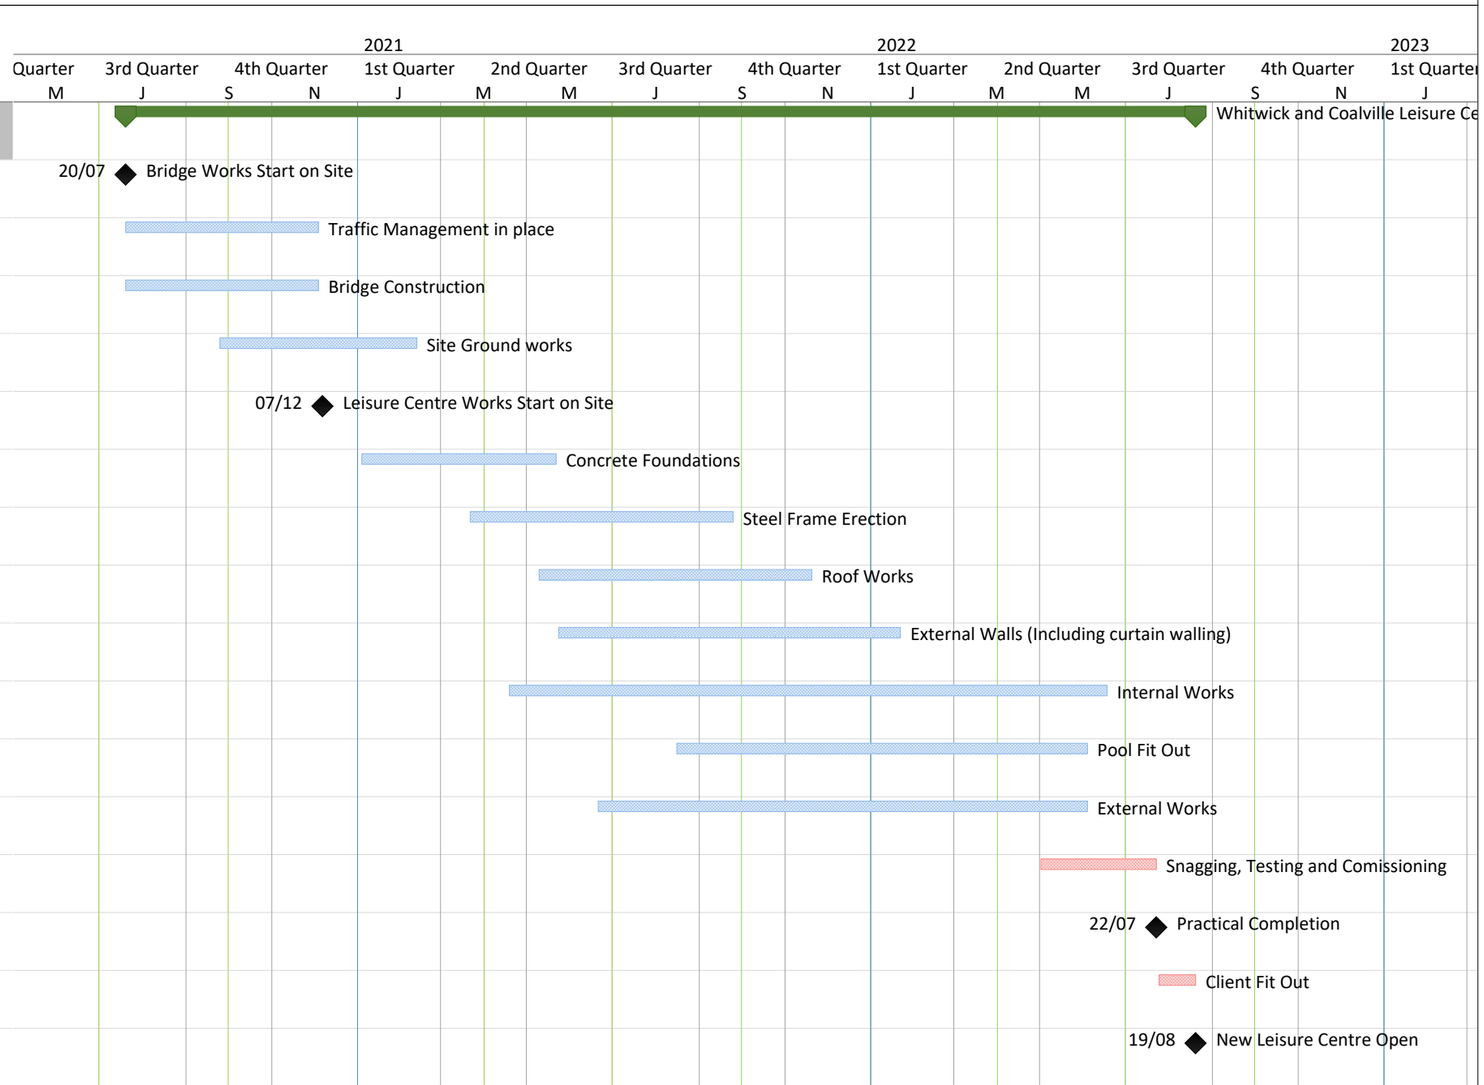
ID	Task Name	Duration	Start	Finish
1	Whitwick and Coalville Leisure Centre	109.2 wk	Mon 20/07/20	Fri 19/08/22
2	Bridge Works Start on Site	0 wks	Mon 20/07/20	Mon 20/07/20
3	Traffic Management in place	20 wks	Mon 20/07/20	Thu 03/12/20
4	Bridge Construction	20 wks	Mon 20/07/20	Thu 03/12/20
5	Site Ground works	20 wks	Fri 25/09/20	Thu 11/02/21
6	Leisure Centre Works Start on Site	0 days	Mon 07/12/20	Mon 07/12/20
7	Concrete Foundations	20 wks	Mon 04/01/21	Fri 21/05/21
8	Steel Frame Erection	27 wks	Mon 22/03/21	Fri 24/09/21
9	Roof Works	28 wks	Mon 10/05/21	Fri 19/11/21
10	External Walls (Including curtain walling)	35 wks	Mon 24/05/21	Fri 21/01/22
11	Internal Works	61 wks	Mon 19/04/21	Fri 17/06/22
12	Pool Fit Out	42 wks	Mon 16/08/21	Fri 03/06/22
13	External Works	50 wks	Mon 21/06/21	Fri 03/06/22
14	Snagging, Testing and Comissioning	12 wks	Mon 02/05/22	Fri 22/07/22
15	Practical Completion	0 days	Fri 22/07/22	Fri 22/07/22
16	Client Fit Out	4 wks	Mon 25/07/22	Fri 19/08/22
17	New Leisure Centre Open	0 days	Fri 19/08/22	Fri 19/08/22
